Mob.: 7873090799 / 9437289832

M/S. BHARAT KUMAR SAHOO

(Consultant Electrical Engineer & Contractor)

(An ISO 9001:2008 Certified)

At./Po./Via.: Rengali Dam Site, Dist.: Angul (Odisha) - 759105

PAN - AQEPS9899P
TIN - 21241307669
Civil (L) - 16808

Email - bharatkumarsahoo99@gmail.com

EPF - 16036
S. Tax - AQEPS9899PSD002
Elect. (L) - 2158 (HT)

Ref No. ORI/BKS/2141 Date. 16/09/2015

To

The Managing Director,

Odisha Knowledge Corporation Ltd.,
Bhubaneswar.

Subject: Verification report of ICT lab

Dear Sir,

We are a registered contractor***M/s.Bharat Kumar Sahoo***, an approved Electrical contractor of Government of Odisha, bearing Licence No. 2158(HT)(Copy of license is enclosed) for your kind perusal.

After verification of the following items of the ICT lab ***GOVT. UPGRADED HIGH SCHOOL, SUNAMUNDA, UDISE Code-*** **21040220401** Block-Tileibani, District-Deogarh, as per the minimum specification mentioned below, the report for the same is being attached.

Sr. No.	*Item name*	*Minimum Specifications*	*Quantity*
1	Earthing (as per IS specifications)	Copper plate earthing stations making earthing with copper earth plate	1
		600 mm x 600 mm x 3 mm thick including funnel, charcoal/coke, salt, all earth work.	
2	Switches and sockets (ISI Mark)	5 A- 240 V switches (Including Switch Board)	15+9=24
		5 in 1 5A and 15A Sockets	19+1=20
		15 A – 240 V socket with shutter	1
		Indicative Brands: - Anchor / Havells / crabtree /Wipro /Phillips / Legrand (Pls. tick) Switches and sockets is to be provided for all electronics/IT equipment including printer and Projection System to be placed at lab technician table.	Havells/ Anchor
3	Wiring (ISI Mark)	PVC conduits including MS/GI boxes. All wires should be covered, insulated and properly clamped. Wiring for 5 and 15A power outlets with 4 square mm PVC insulated stranded copper conductor wires Earthing of 3rd pin with PVC insulated green color 2.5 square mm copper wire	Full Lab

With regards
Name & Signature with seal

FORM 'D'

(Regulation 28)

ELECTRICAL CONTRACTOR'S LICENSE

This license is to be renewed for a period of three years at a time and must be produced on demand by the Secretary.

2

(Not transferable or renewable by any authority other than the Electrical Licensing Board of Orissa)

I do hereby certify that Messers/Shri Bharat Kumar Sahoo have this day been granted license to carry out electrical installation work of the following class/classes in the State of Orissa for the purpose of Rule 45 (I) of Indian Electricity Rules, 1956.

Name and address of the person/ firm to whom license is issued. At/po-Rengali Dam Site. Dist-Angul.

Date of approval by Electrical Licensing Board, Orissa. To be ratified

Date of issue of license 09.02.2011

Type of electrical installation work for which license is issued. Allowed to Execute. Electrical installation works up to 11 kv (Without cable jointing)

Registration No. 2158 (Hft) 9/2/11

Electrical Inspector to the Government of Orissa and Secretary, Electrical Licensing Board, Orissa.

Bharat Kumar Sahoo
Boss

Asst. Executive Engr. (Elect.)
O/O The E.I (Hqr)-cum-Secy,
E.L.B.O, Bhubaneswar

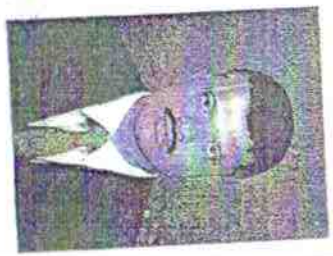

LICENSE FOR
ELECTRICALCONTRACTOR

Bharat Kumar Sahoo
At/po-Rengali Damsite
Dist-Angul

2158 (Hft)

Executive Engineer(Elect)
O/O The Chief Electrical Inspector
(T&D) Orissa, BBSR

Date of Renewal	Date of Expiry	Signature of the Electrical Inspector and Secretary, Electrical Licensing Board, Orissa
(1)	(2)	(3)
Allowed to ...HT works upto 33KV. (Without cable jointing)	Execute Electrical installation ... 2/5/11 SECRETARY E L B O	
Ratified in 1.8.11.	130th Meeting of ELBO held on	

Present Status	Validity
1. I.K Path. S/CC/CB/NO 7636	17.12.2014.
2. S.K Samantaray. L/M-A/NO-RKL-1089.	4.3.2015
3. N.C Mohanty. W/M-B/NO-BHL-554.	03.03.2016.
4. P.K Harnayak W/M-B/NO-AHL-1507.	29.5.2016
5. S. Samal W/M-C/NO-AHL-1524.	29.5.2016

18/4/12 SECRETARY E L B O

Not renewed from 7.2.2012 to 12.2.2012 and renewed from 13.02.2012 - 06.02.2015

18/4/12 SECRETARY E L B O 18/4/12

Date of Renewal	Date of Expiry	Signature of the Electrical Inspector and Secretary, Electrical Licensing Board, Orissa
Present Status (1)	(2)	Validity (3)
1. I.K Path. S/CC/CB/NO 7636.	17.12.2011	
2. S. Sahu L/M-B/NO-RKL-248.	04.02.2014.	
3. N.C Mohanty W/M-B/NO-AHL-554	03.03.2011/2016	
4. P.K Harnayak W/M-B/NO-AHL-1507.	29.5.2011	
5. S. Samal W/M-C/NO-AHL-1524	29.5.2011	
LT - SL/NO 34227. CIB Make - 1000V		
BT - SL/NO. 2000 7308 CIB Make		

9/2/11 SECRETARY

PROVISIONALLY ALLOWED FOR 1 YEAR i.e. FROM 07.02.2011 TO 06.02.2012 SUBJECT TO RATIFICATION BY E.L.B.O.

9/2/11 SECRETARY E L B O

S.K Samantaray. L/M-A/NO-RKL-1089. V - 04.03.2015

Allowed to Execute Electrical installation upto 33KV (Without Cable Jointing)

9/2/11 SECRETARY E L B O

2/5/11

Present status.

	Validity
1. J K Rath S.C (HT) No. 7636.	17.12.2017
2. S.K Pradhan M/M-HT No AHL-1682	12.5.2018
3. N.C Mohanty. M/M-MV No AHL-554.	03.03.2016
4. P.K Harchayak M/M-MV No. AHL 1507	29.5.2016
5. S. Samal L/M-MV No AHL-2086	11.9.2017

Not renewed from 7.2.2015 to 01.05.2015 and renewed from.

(Cancelled is invalid from 5.3.15 to 8.4.15)

02.05.2015 - 06.02.2018

30.05.2015

SECRETARY
E.L.B.O, ODISHA
